


Knowledge Commons Update

Al Williams


August 21, 2011

<http://tinyurl.com/alwkcupdate>




Objectives

- ▶ Focus on collaborative learning
- ▶ Provide Multimedia Resources
- ▶ One Stop place to get information
- ▶ Student computing resources
 - Better storage for supplies
- ▶ MTSS moves in from Willard




Original Time Line

- ▶ Finish Pattee West by Fall 2011
- ▶ Renovate Gateway by end of Fall 2011 semester
- ▶ Whole project done before Christmas 2011




Slight Problem

- ▶ Floors in Pattee West need reinforcement
- ▶ Draw up new plan
- ▶ Set new timeline




New Targets

- ▶ Pattee West done for Spring Semester
- ▶ Start Gateway after Pattee West done
- ▶ Gateway done by mid-March 2012
- ▶ Other projects still on schedule
 - New Lending Services in Weltman Lobby
 - Sidewater Lobby (aka train station) finish by November
 - Adaptive Services finish by end of October




Old Printer Supplies




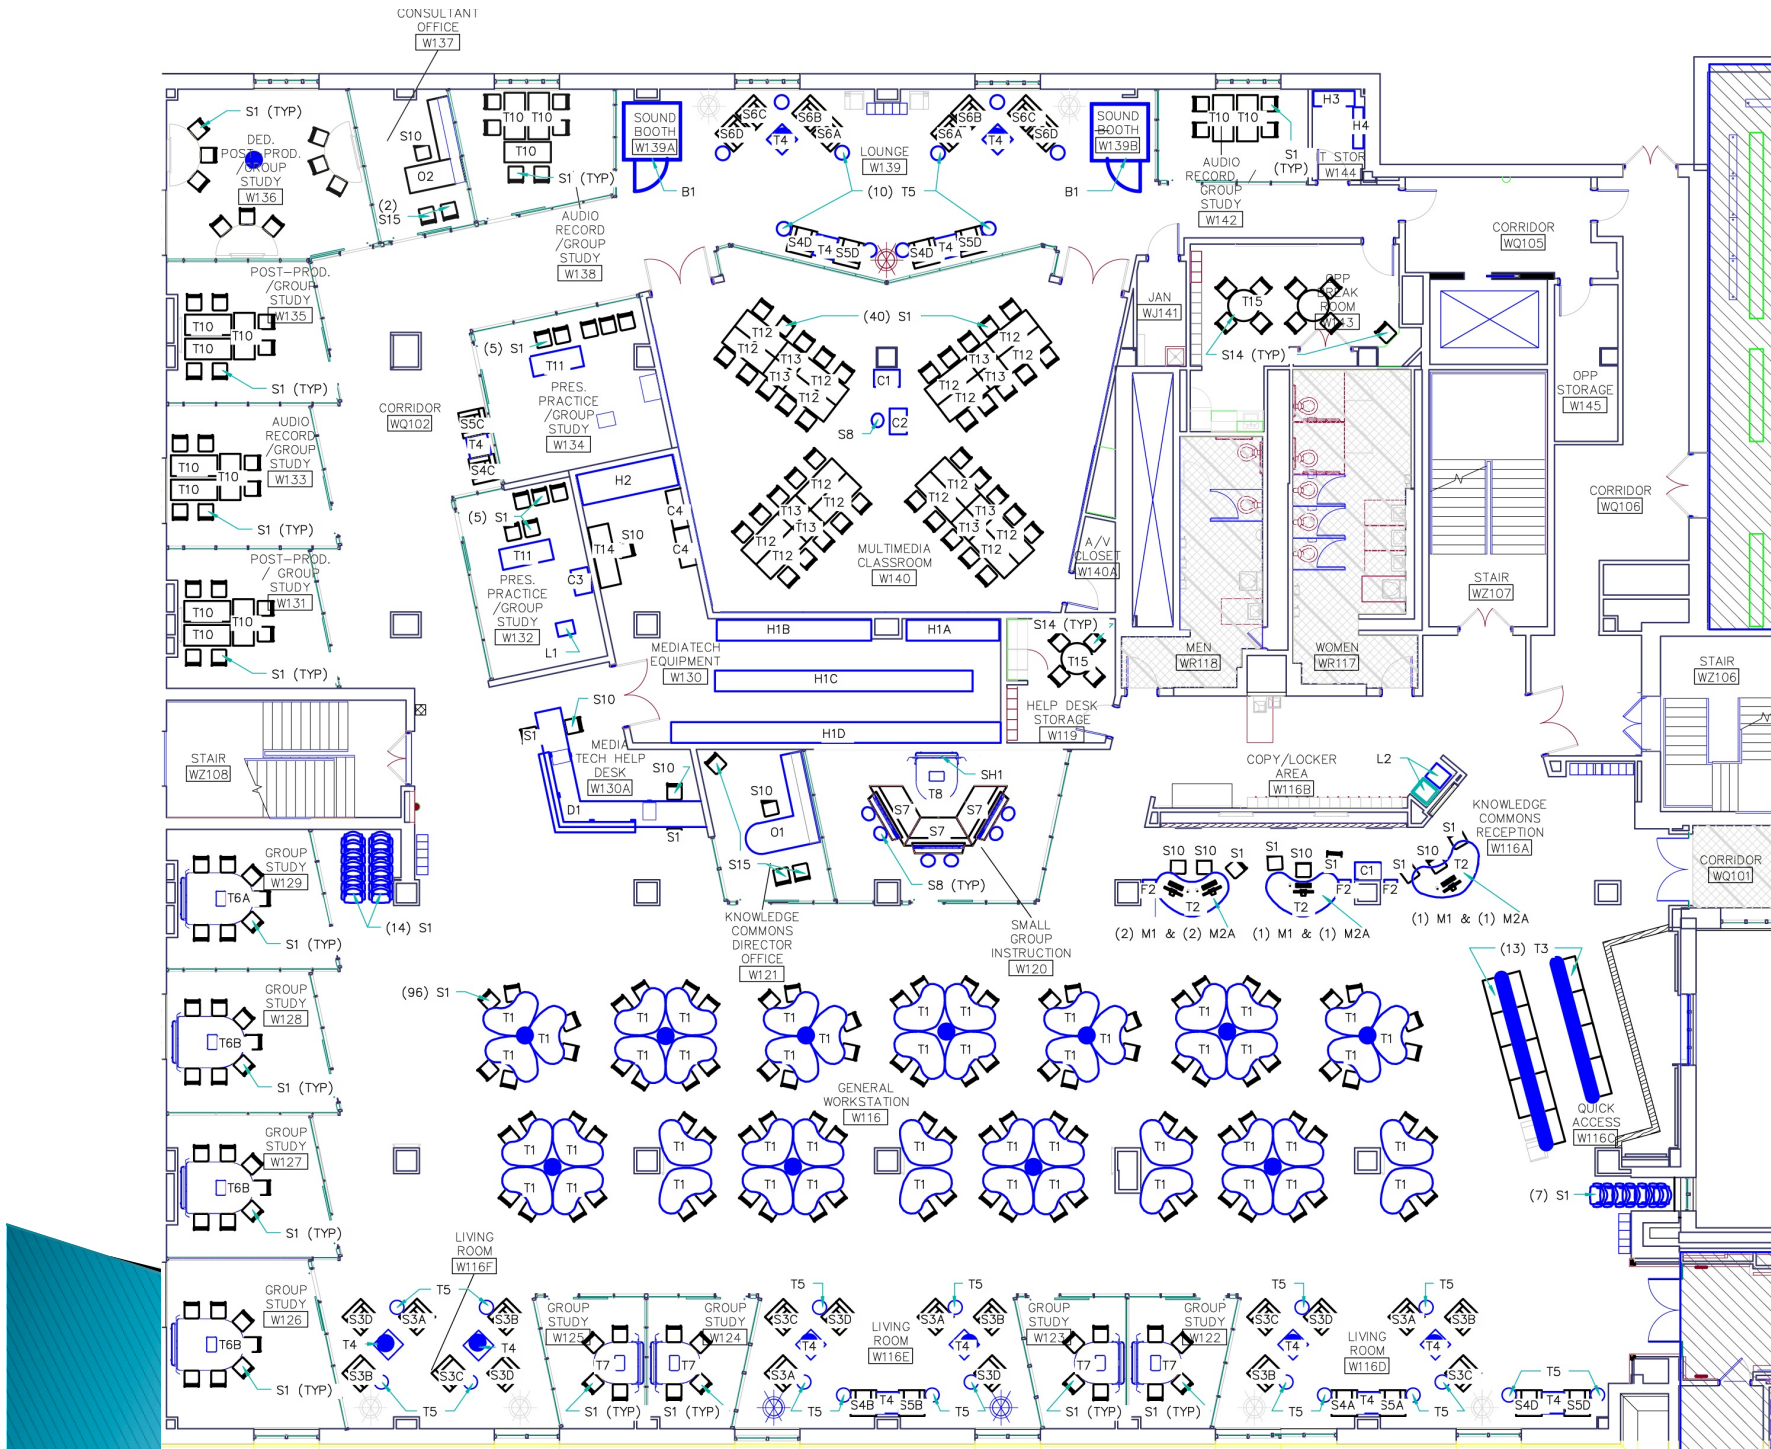


KC West Student Computing

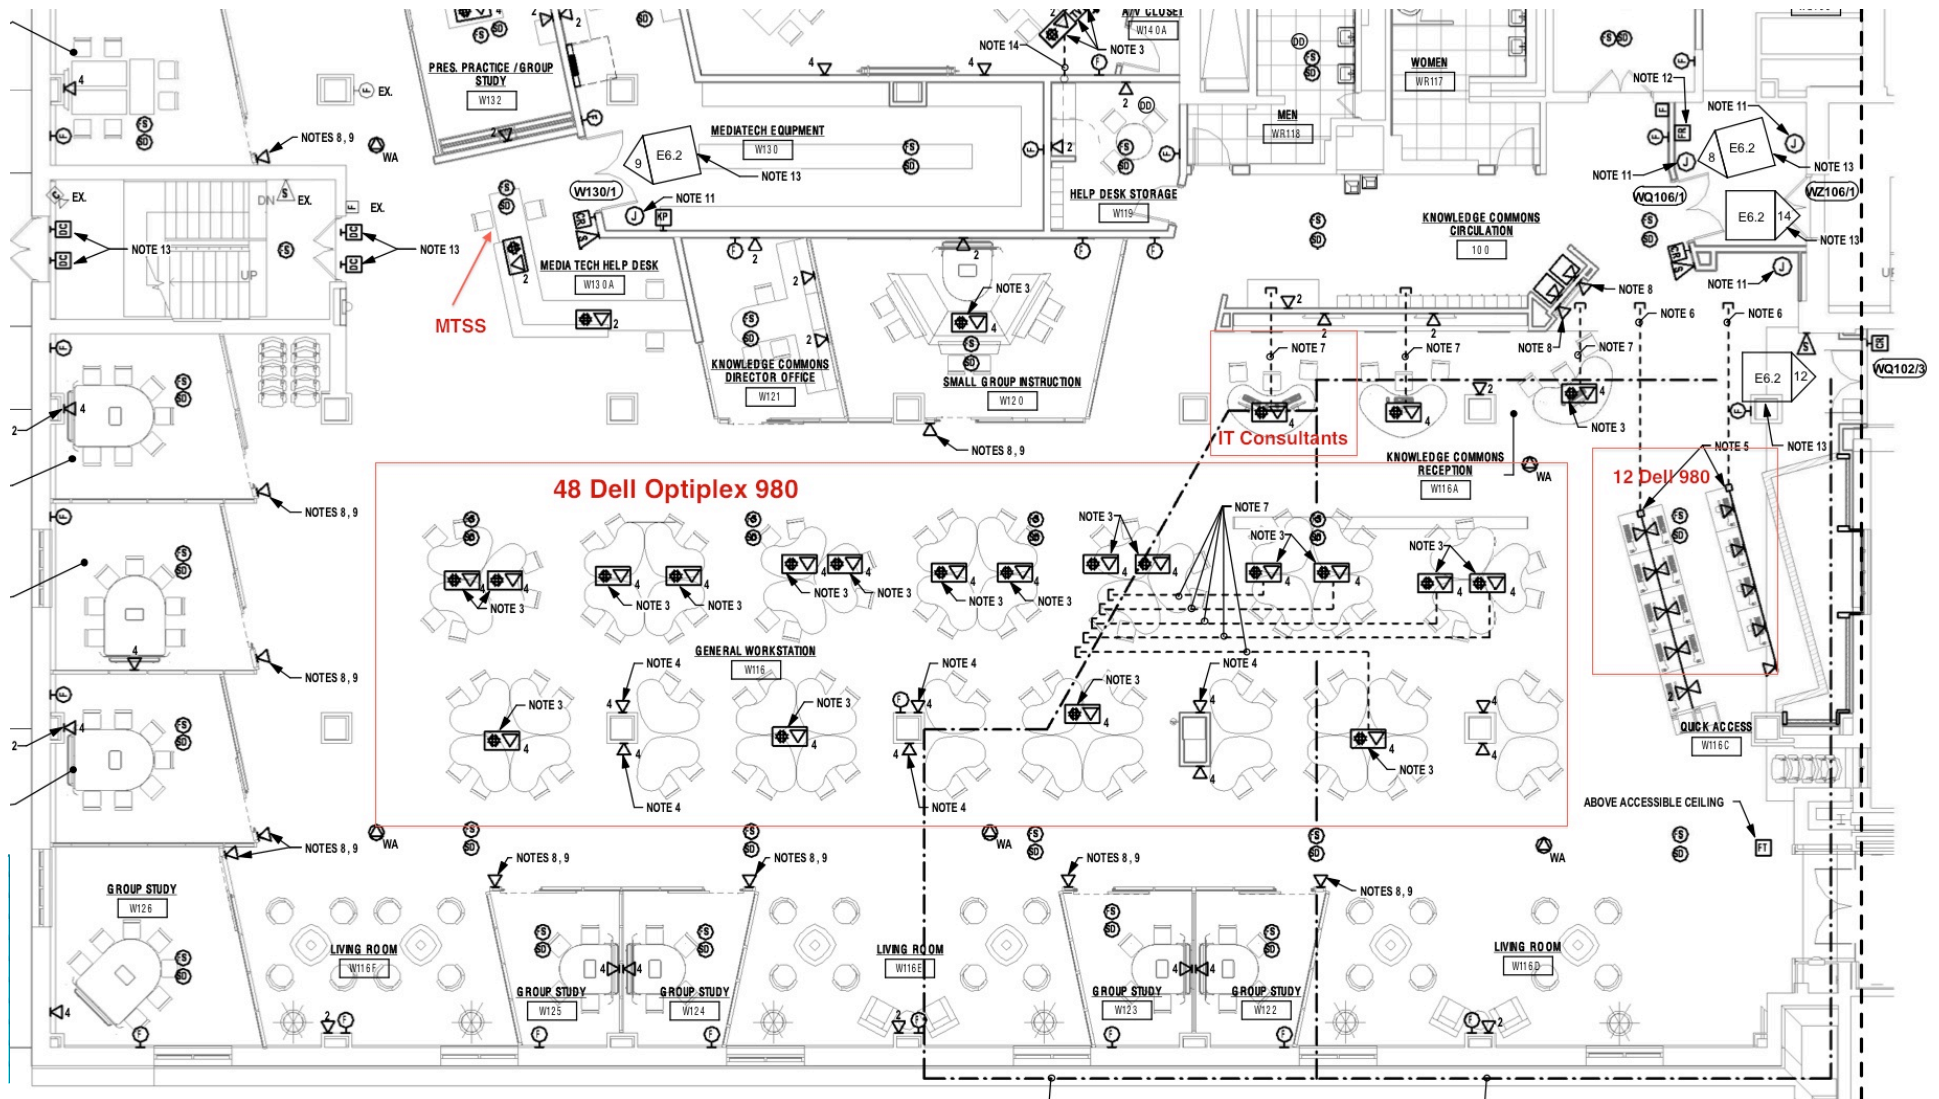


West Pattee

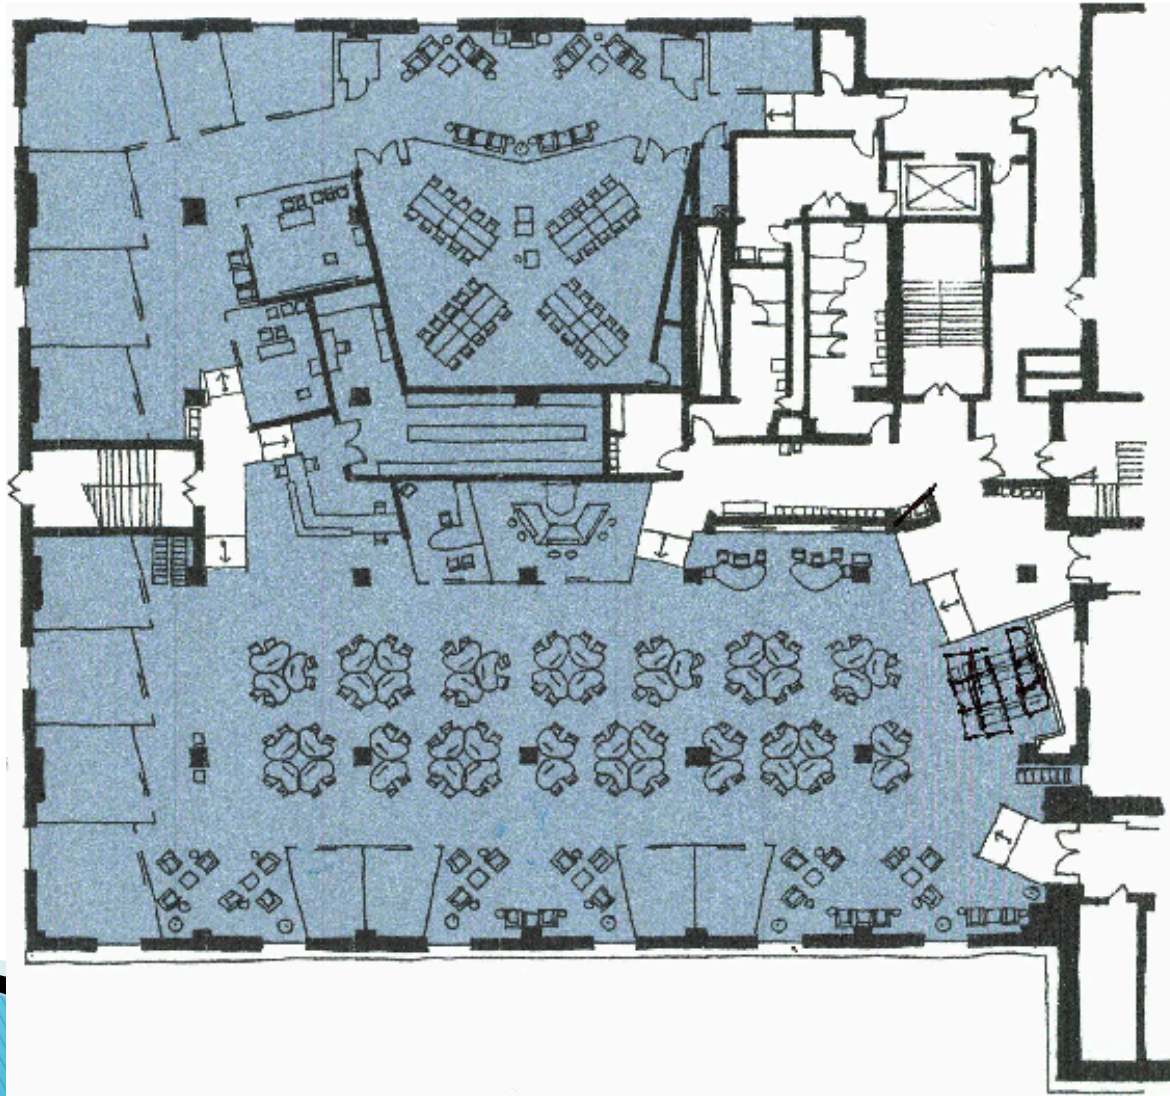



Pattee Central

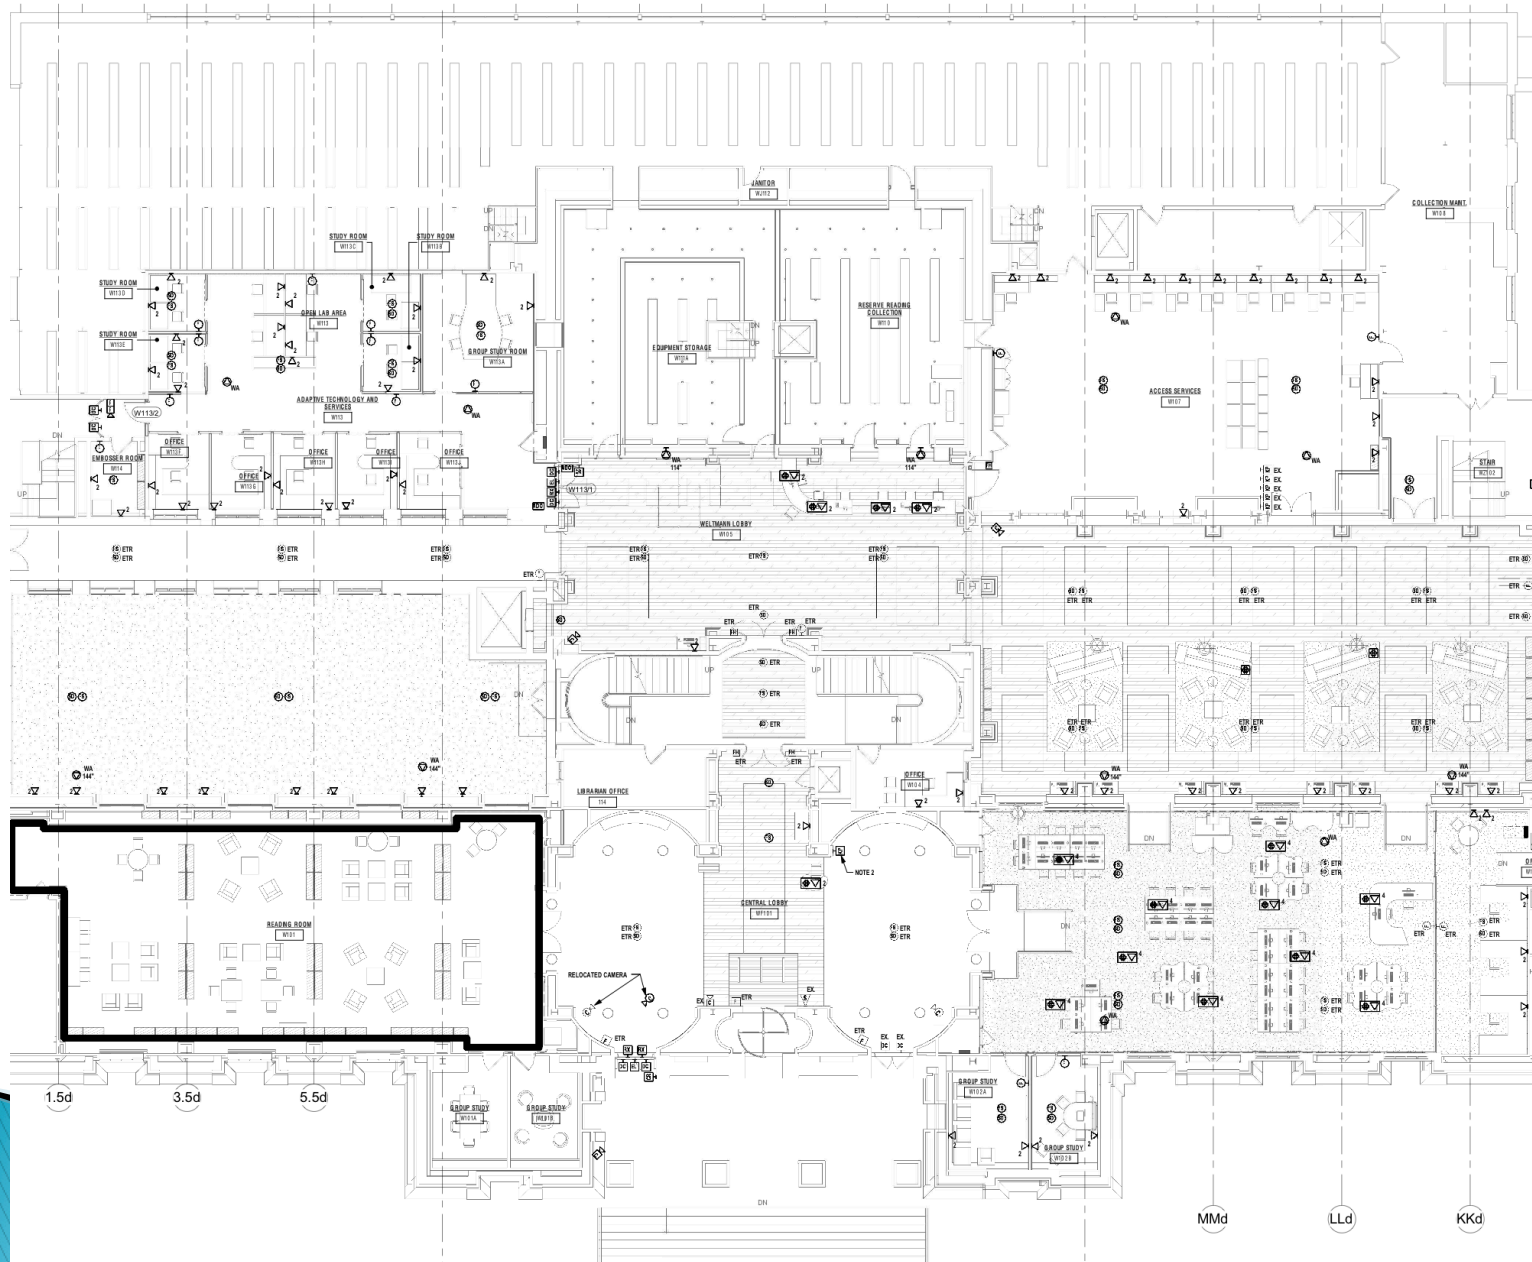

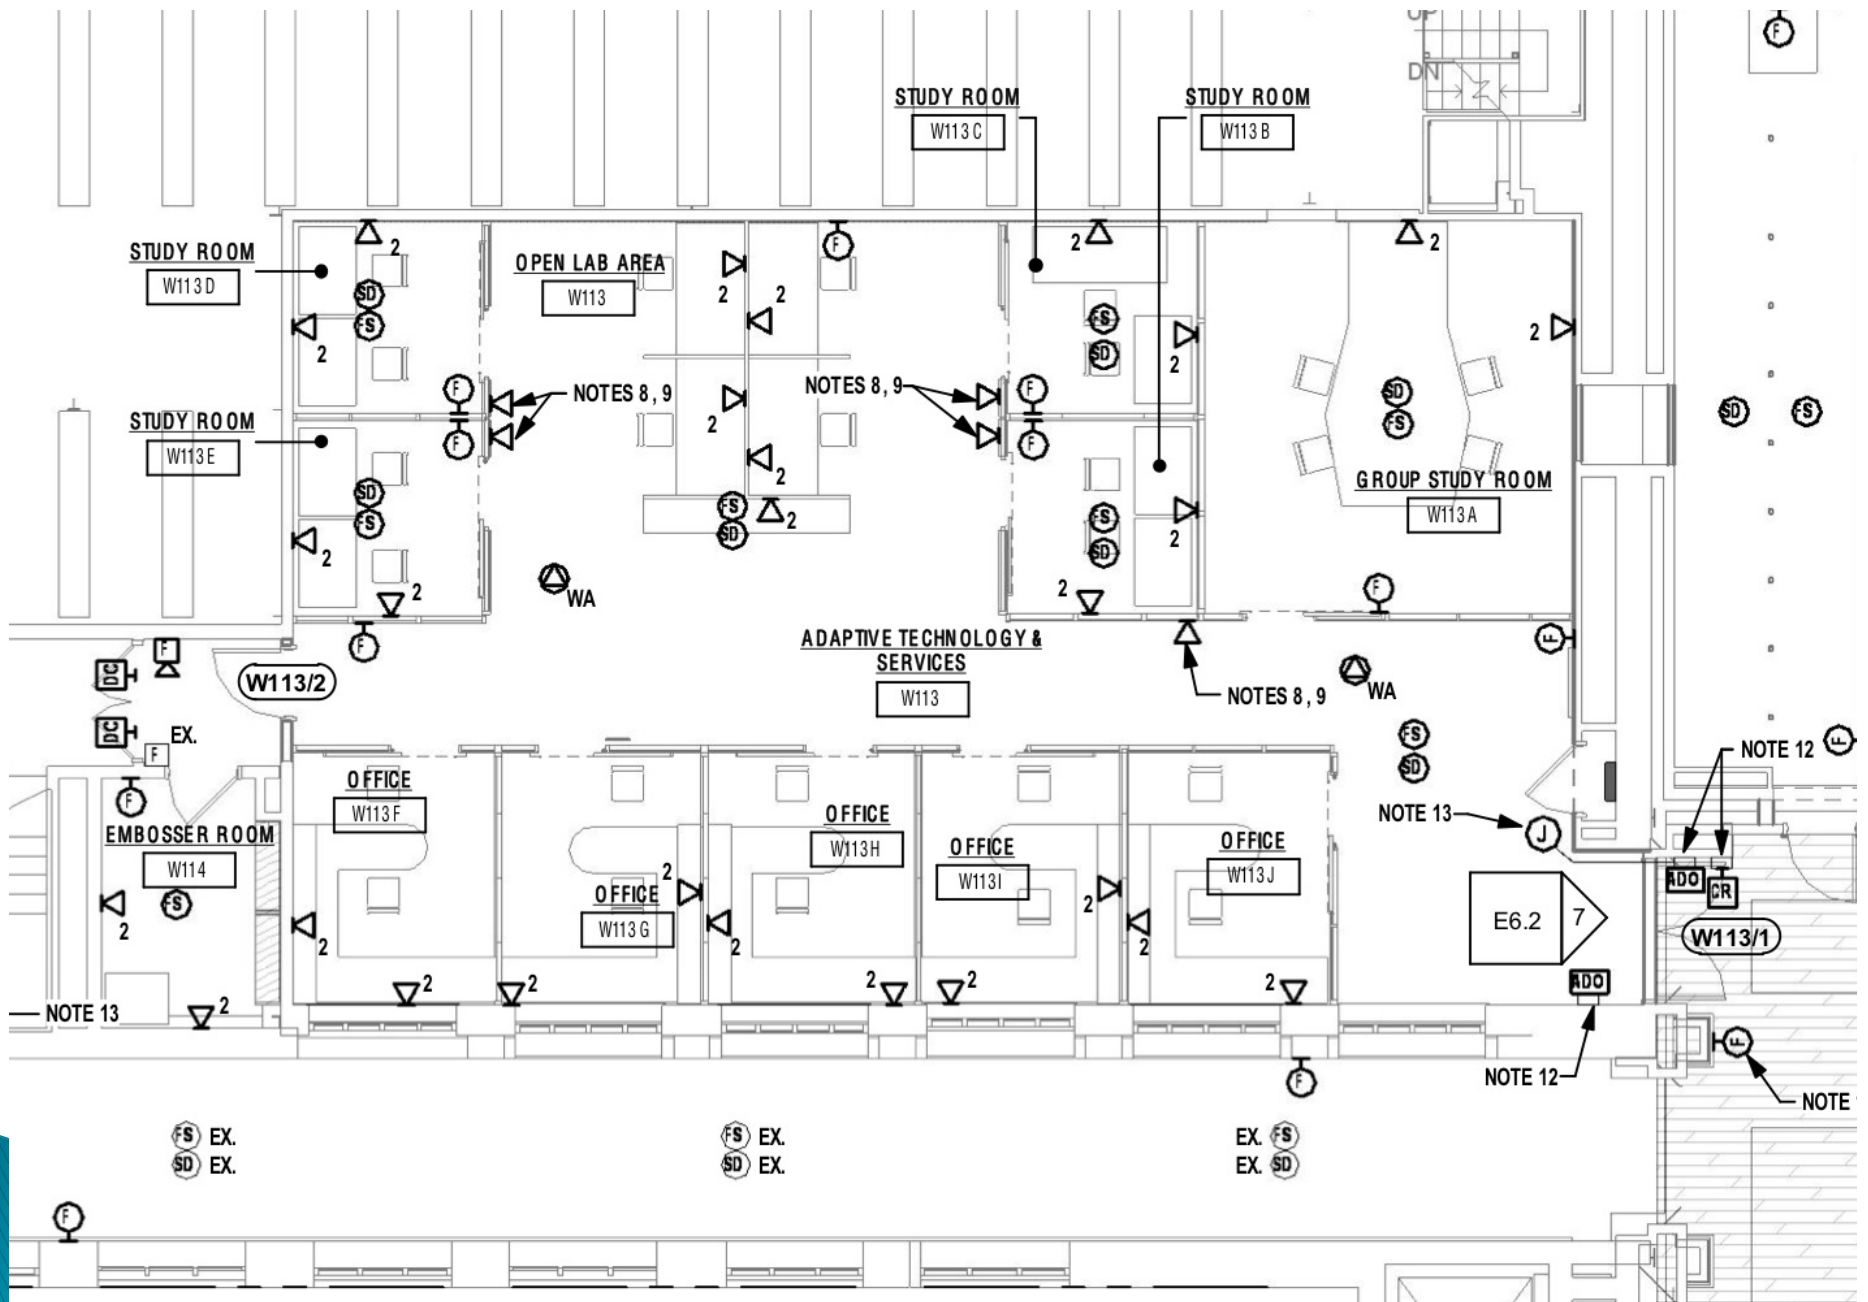


Current Gateway Lab

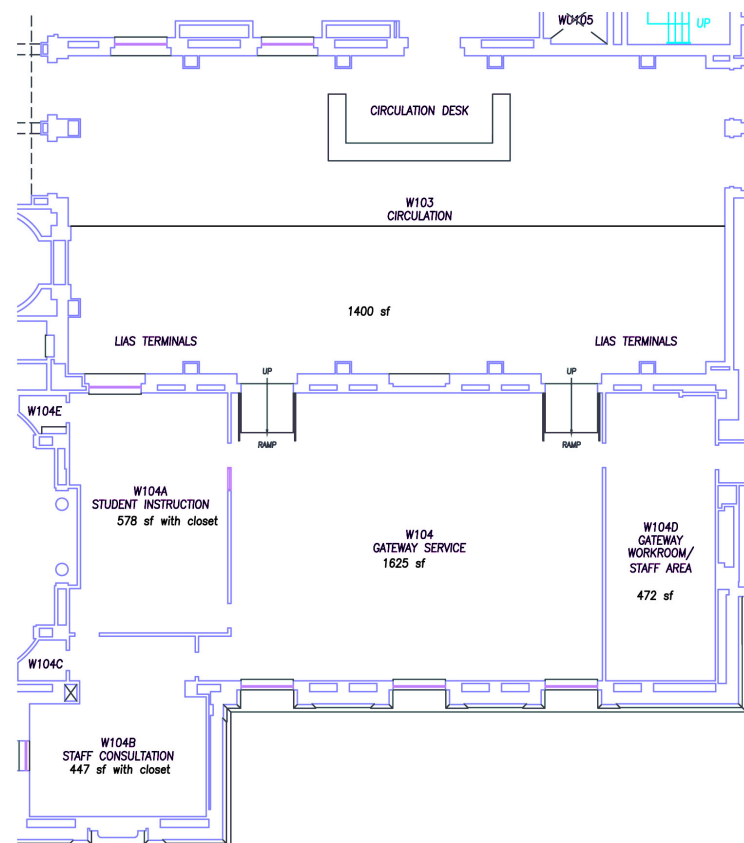

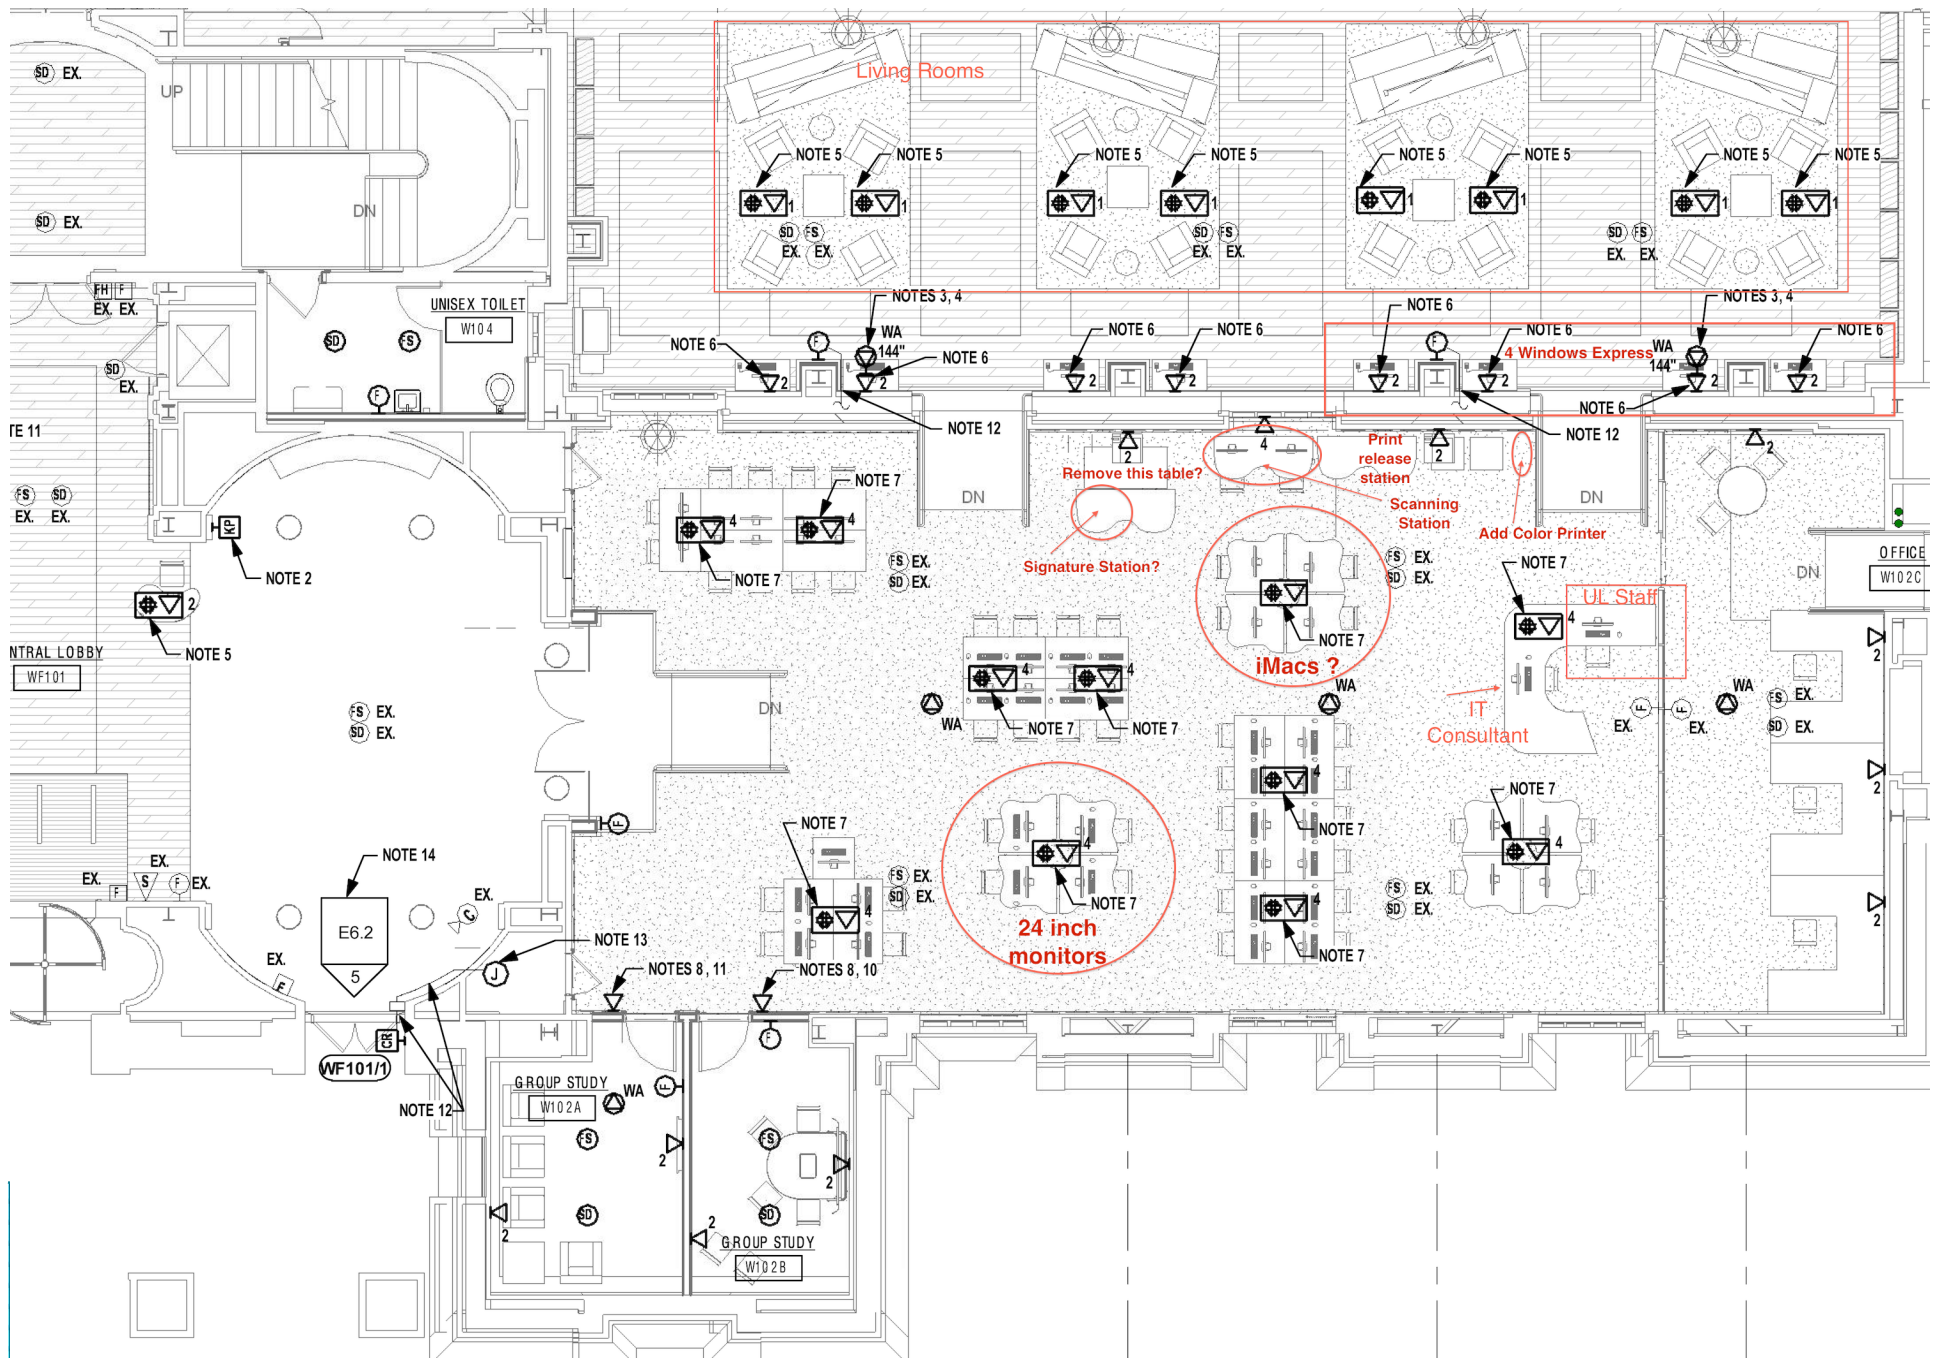

Pattee Library Knowledge Commons

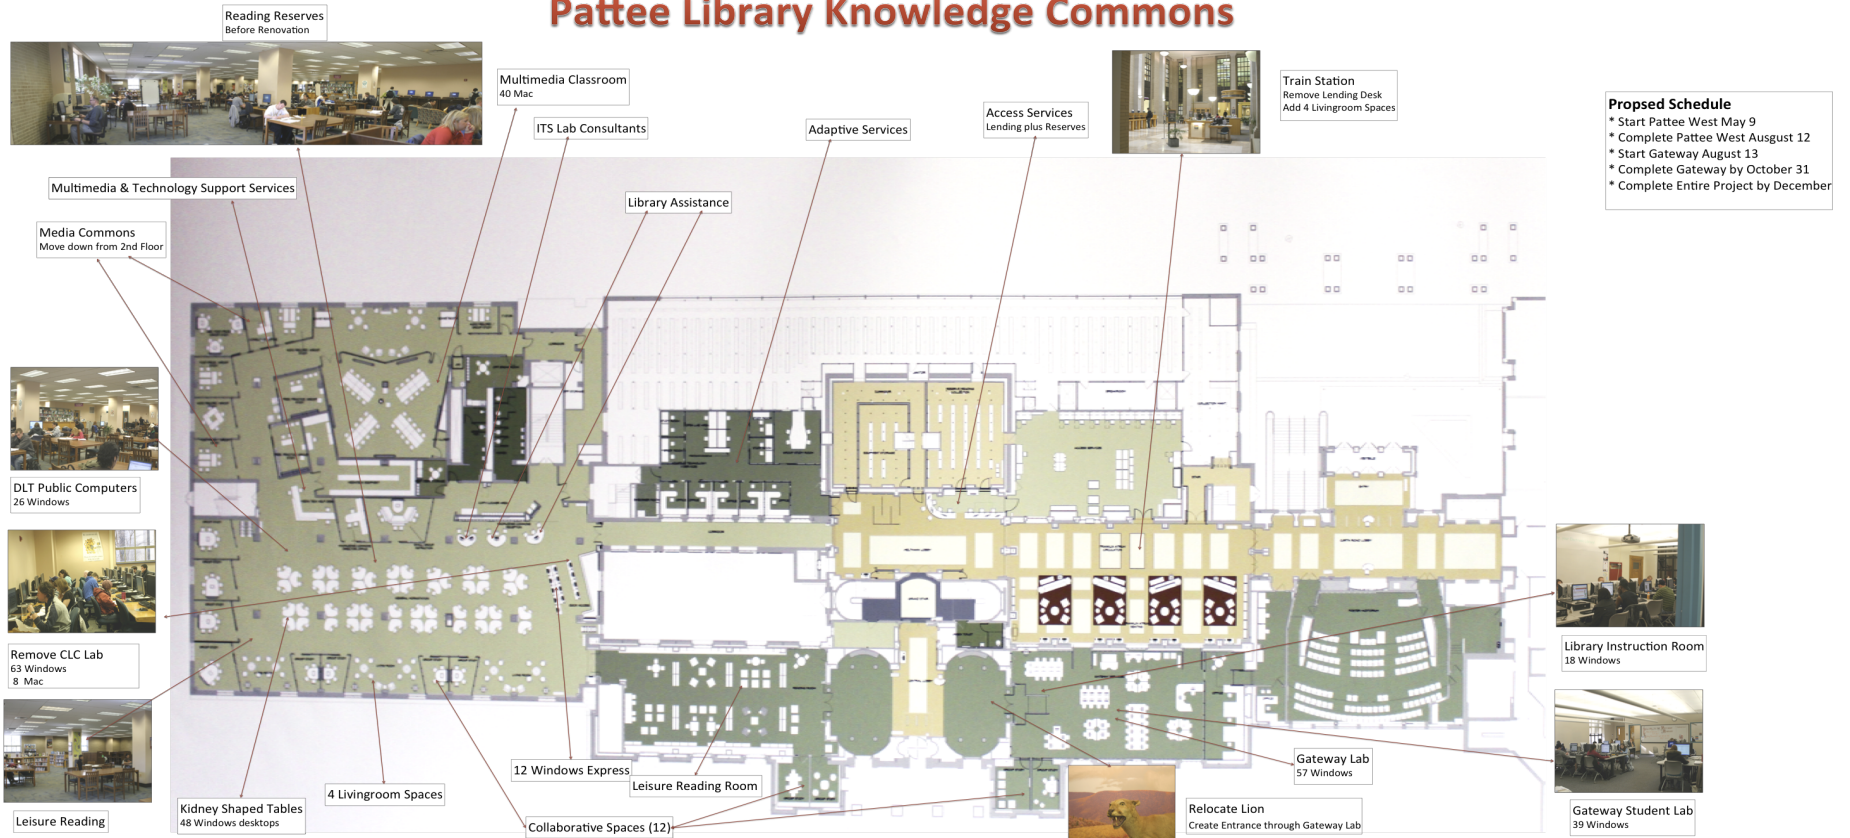

Questions?

